1st & Final bill

Recorded on:-

Job Code NO:- 002-21-000013

Est Cost: 125.00 Lakhs

369446

M. A. R. 57 (Rule 116) No. E

Measurement Book

Work order NO: BBMP/EE YNK.D/EPMT-08/00/08/2021-22

Serial No. .....

Name of work Construction of Rain water head of drains at Kondappa Layout 19th to 28th Cross in Chowdeshwari ward NO-02.

Name of Contractor of nature of Agency Sri Gopi Reddy S/o Muni Reddy. #03, 1st main, 1st Cross, Ramachandrappa Layout, Veerannapalya, Near Arabic College Bangalore 560045.

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	(1) KSRRB 300 - Excavation for road drains and similar works. KSRRB 300-1, Earth work excavation by manual means in ordinary soil involving an average horizontal throw up to 2 meters and an average lift up to 0.5 m, excavated surface levelled and sides neatly dressed, The disposed earth to be levelled mostly after breaking of clods Complete as per Specifications. MORTH/chapter 3 (P.NO-143, IND-19.1). Quantity vide, As per prepared in excel sheets:- 1665.90 m^3 CRS. 144.55					2,40,805.34	
	(2) KSRB 2-4: Refilling available earth around pipelines, Cables in layers not exceeding 20 Cms in depth, Compacting each deposited layer by						

M. A. R. 57 (Rule 116) No. E 369448
Measurement Book

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Quantity vide, AS per prepared in excel sheets:- 292.84 m³ @Rs. 7416.64 21,71,915.19						
	⑥ KSRRB - on 2300-14: Providing TMT Steel reinforcement for R.C.C work including straightening, cutting, bending, hooking placing in position lapping and/or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary Complete as Per design (laps, hooks and wastage shall not be measured and paid) Cost of materials, labours, Hire of machinery Complete as per Specifications. MORTH Specification NO. 1600 & 2200 for TMT bars Fe 500.						
	(P.NO. 239, I NO. 29.29.2 of PW, P&IWTD SR 2018-19)						

M. A. R. 57 (Rule 116) No. E 369451

Measurement Book

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
					12% GST :-		13,16,081.02
					Total :-		1,22,82,765.00

Verified 5/8/2021
AE-02

CERTIFICATE :-

① Certified that the above work done is satisfactory completed.

② Certified that the there is no debrics have been cleared to site.

Verified 5/8/2021
AE-02

Asst. Executive Engineer 5/8/21
Yelahanka Sub. Division
(BBMP Ynk. Zn)
Yelahanka, Bangalore

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents
		Number	Length	Breadth	Depth	
1	2	3	4	5	6	7

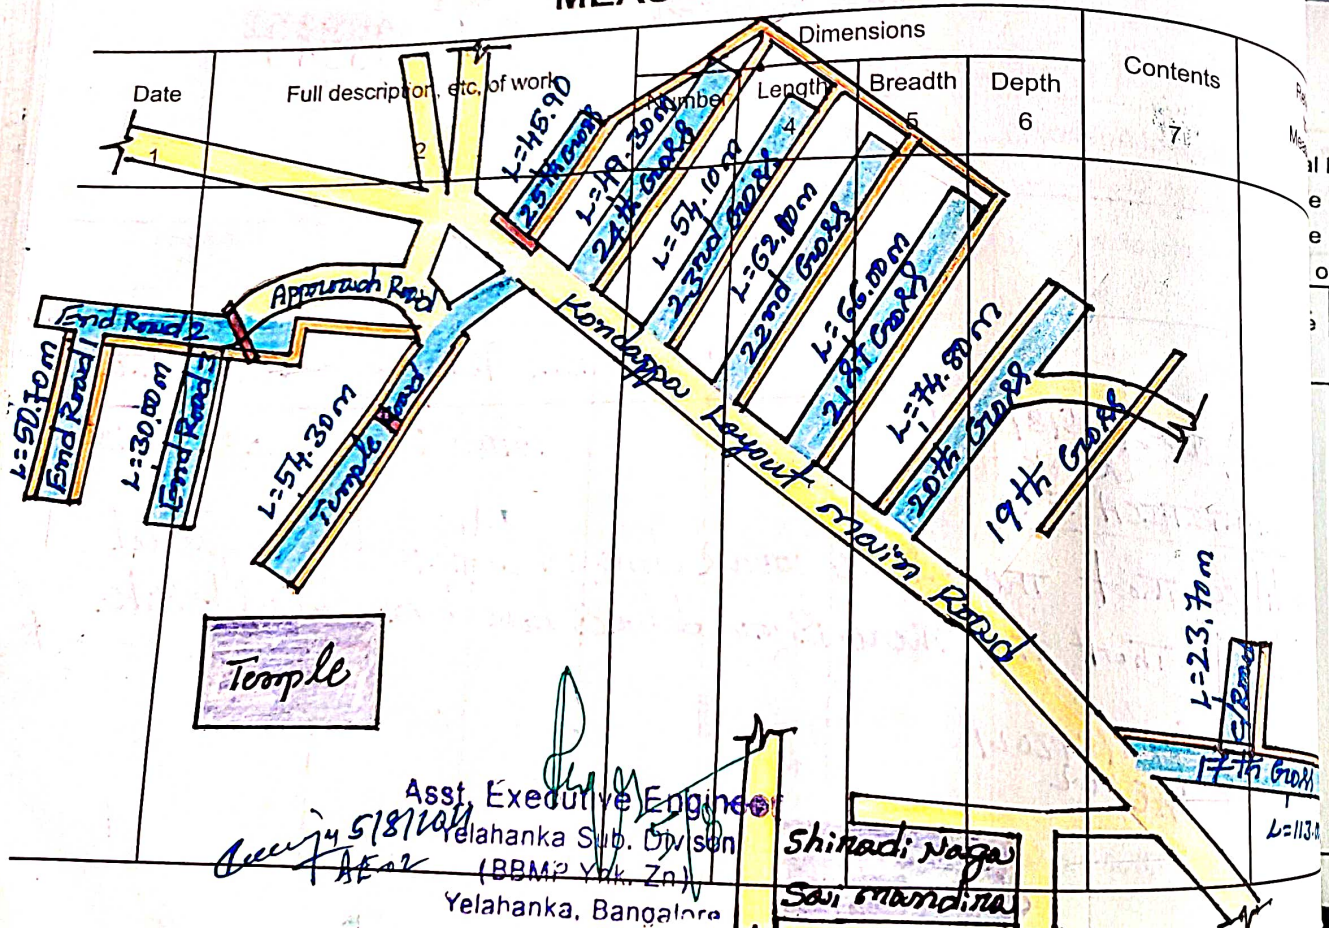

M. A. R. 57 (Rule 116)
Measurement Book

No. E

3

al No. .....

e of work ..... From ..... To .....

e of Contractor of nature of Agency.....

of commencement of work.....

Full description, etc, of work	Dimensions				Contents
	Number	Length	Breadth	Depth	
2	3	4	5	6	7

INDEX:-

- C.C Road
- culverts
- C.C Drain
- Locations
- Existing Road

Asst. Executive Engineer
Yelahanka Sub. Division
(BBMP Ynk. Zn)
Yelahanka, Bangalore
5/8/2024
